

Well no : 6507/07-07 X

Operator : CONOCO

Coordinates : 65 17 52.25 N
07 18 50.65 E

UTM coord. : 7242882 N
421386 E

Licence no : 95

Permit no : 546

Rig : HUNTER

Rig type : SEMI-SUB.

Contractor : WILHELMSSEN OFFSHORE SERVICES

Bottom hole temperature : deg.C

Elev. KB : 25 M

Spud. date : 87.05.11

Water depth : 335 M

Compl. date : 87.06.07

Total depth : 1035 M

Spud. class : APPRAISAL

Form. at TD :

Compl. class : JUNKED

Prod. form :

Seisloca : CN 8502 - 482 SP. 570

LICENSEES

10.000000	ARCO NORGE A/S
30.000000	NORSKE CONOCO A/S
50.000000	DEN NORSKE STATS OLJESELSKAP A.S
10.000000	TENNECO OIL NORWAY A/S

CASING AND LEAK-OFF TESTS

Type	Casing diam.	Depth below KB	Hole diam.	Hole depth below KB	Lot mud eqv. g/cm3
CONDUCTOR	30	458.0	36	525.0	1.02

MUD PROPERTIES

Depth below KB meter	Mud weight g/cm3	Viscosity	Mud type
1034.000	1.04	0.0	WATER BASED
1035.000	1.04	0.0	WATER BASED
1035.000	1.04	0.0	WATER BASED

DRILL BIT CUTTINGS AND WET SAMPLES

SAMPLE TYPE	INTERVAL BELOW KB	NUMBER OF SAMPLES
-------------	-------------------	-------------------

Cutting

Wet Samples

SHALLOW GAS


Interval below KB	REMARKS
-------------------	---------

AVAILABLE LOGS

<i>LOG TYPE</i>	<i>INTERVALS</i>	<i>1/200</i>	<i>1/500</i>	<i>Div.</i>
<hr/>				
<i>BRØNNEN ER IKKE LOGGET</i>				<i>TD:1035 M.</i>

DAILY DRILLING REPORT SYSTEM

MAIN OPERATIONS FOR WELL: 6507/07-07

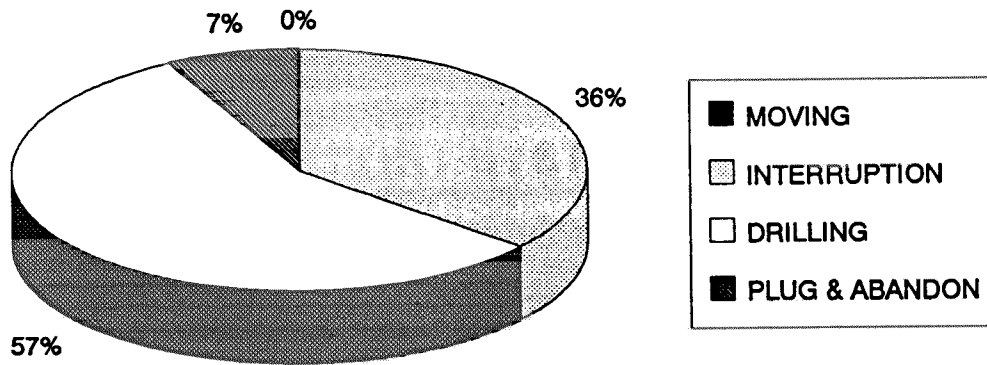

Main operation	Minutes	Hrs	% of total
MOVING	30	0,5	0,07
INTERRUPTION	14580	243,0	36,16
DRILLING	22740	379,0	56,40
PLUG & ABANDON	2970	49,5	7,37
<i>Total</i>	40320	672,0	100,00

SUB OPERATIONS FOR WELL: 6507/07-07

MAIN OPERATION: MOVING

Sub operation	Minutes	Hrs	% of total
ANCHOR	30	0,5	100,00
Total	30	0,5	100,00

MAIN OPERATION: INTERRUPTION

Sub operation	Minutes	Hrs	% of total
MAINTAIN/REP	2730	45,5	18,72
FISH	11850	197,5	81,28
Total	14580	243,0	100,00


MAIN OPERATION: DRILLING

Sub operation	Minutes	Hrs	% of total
CASING	3390	56,5	14,91
TRIP	3660	61,0	16,09
DRILL	8670	144,5	38,13
REAM	2940	49,0	12,93
SURVEY	30	0,5	0,13
WAIT	630	10,5	2,77
CIRC/COND	450	7,5	1,98
OTHER	930	15,5	4,09
BOP/WELLHEAD EQ	2040	34,0	8,97
Total	22740	379,0	100,00

MAIN OPERATION: PLUG & ABANDON

Sub operation	Minutes	Hrs	% of total
TRIP	960	16,0	32,32
PERFORATE	450	7,5	15,15
SQUEEZE	90	1,5	3,03
OTHER	1020	17,0	34,34
CUT	210	3,5	7,07
EQUIP RECOVERY	210	3,5	7,07
CEMENT PLUG	30	0,5	1,01
Total	2970	49,5	100,00

DEPTH V.S. TIME FOR WELL :

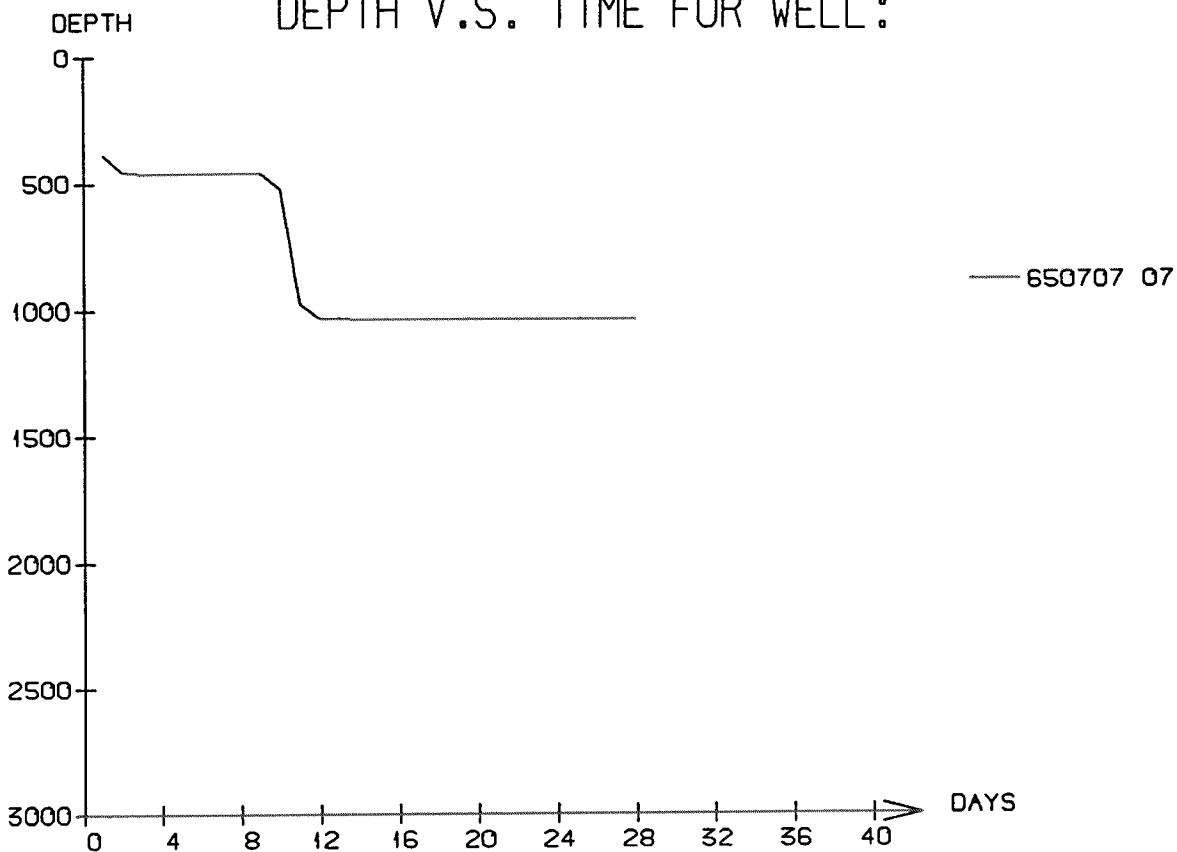

WELL : 650707 07 PRESSURE COMPOSITE PLOT

